

FINAL DRAWING & MATERIAL APPROVAL NOTICE

Production release, client approval and post-approval change procedure

CLIENT	[Client Name]	PROJECT	[Project Name]
ISSUED BY	Guangzhou ONI Shopfitting Limited	DOCUMENT	Final Approval Notice

Dear [Client Name],

Thank you for your cooperation with the [Project Name] project.

Please find attached the latest production/shop drawings and material specifications for your final review and approval.

As we are now approaching the production stage, please carefully review all details before providing final confirmation, including:

- Overall dimensions and individual fixture dimensions
- Construction, structural, shape, profile and design details
- Materials, finishes, colors and surface treatments
- Metalwork, hardware, glass and acrylic specifications
- LED lighting, electrical components and lighting positions
- Openings, fixing points and installation interfaces
- Quantities, item references and all project-specific details shown on the drawings or material schedule

FINAL APPROVAL IS THE FORMAL PRODUCTION RELEASE POINT

1. FINAL APPROVAL PROCEDURE

STEP 1

ONI SUBMISSION

ONI submits the production/shop drawings, material specifications, finish details and other relevant technical documents for review.

STEP 2

CLIENT REVIEW

Please review all drawings and specifications carefully with your project team, designer, contractor and/or site team where applicable.

STEP 3

WRITTEN APPROVAL


Final approval may be provided by signing/stamping each drawing and returning the approved copies, or by written confirmation through email or another agreed formal communication channel.

STEP 4

ONI SUBMISSION

ONI submits the production/shop drawings, material specifications, finish details and other relevant technical documents for review.

PRODUCTION WORKFLOW

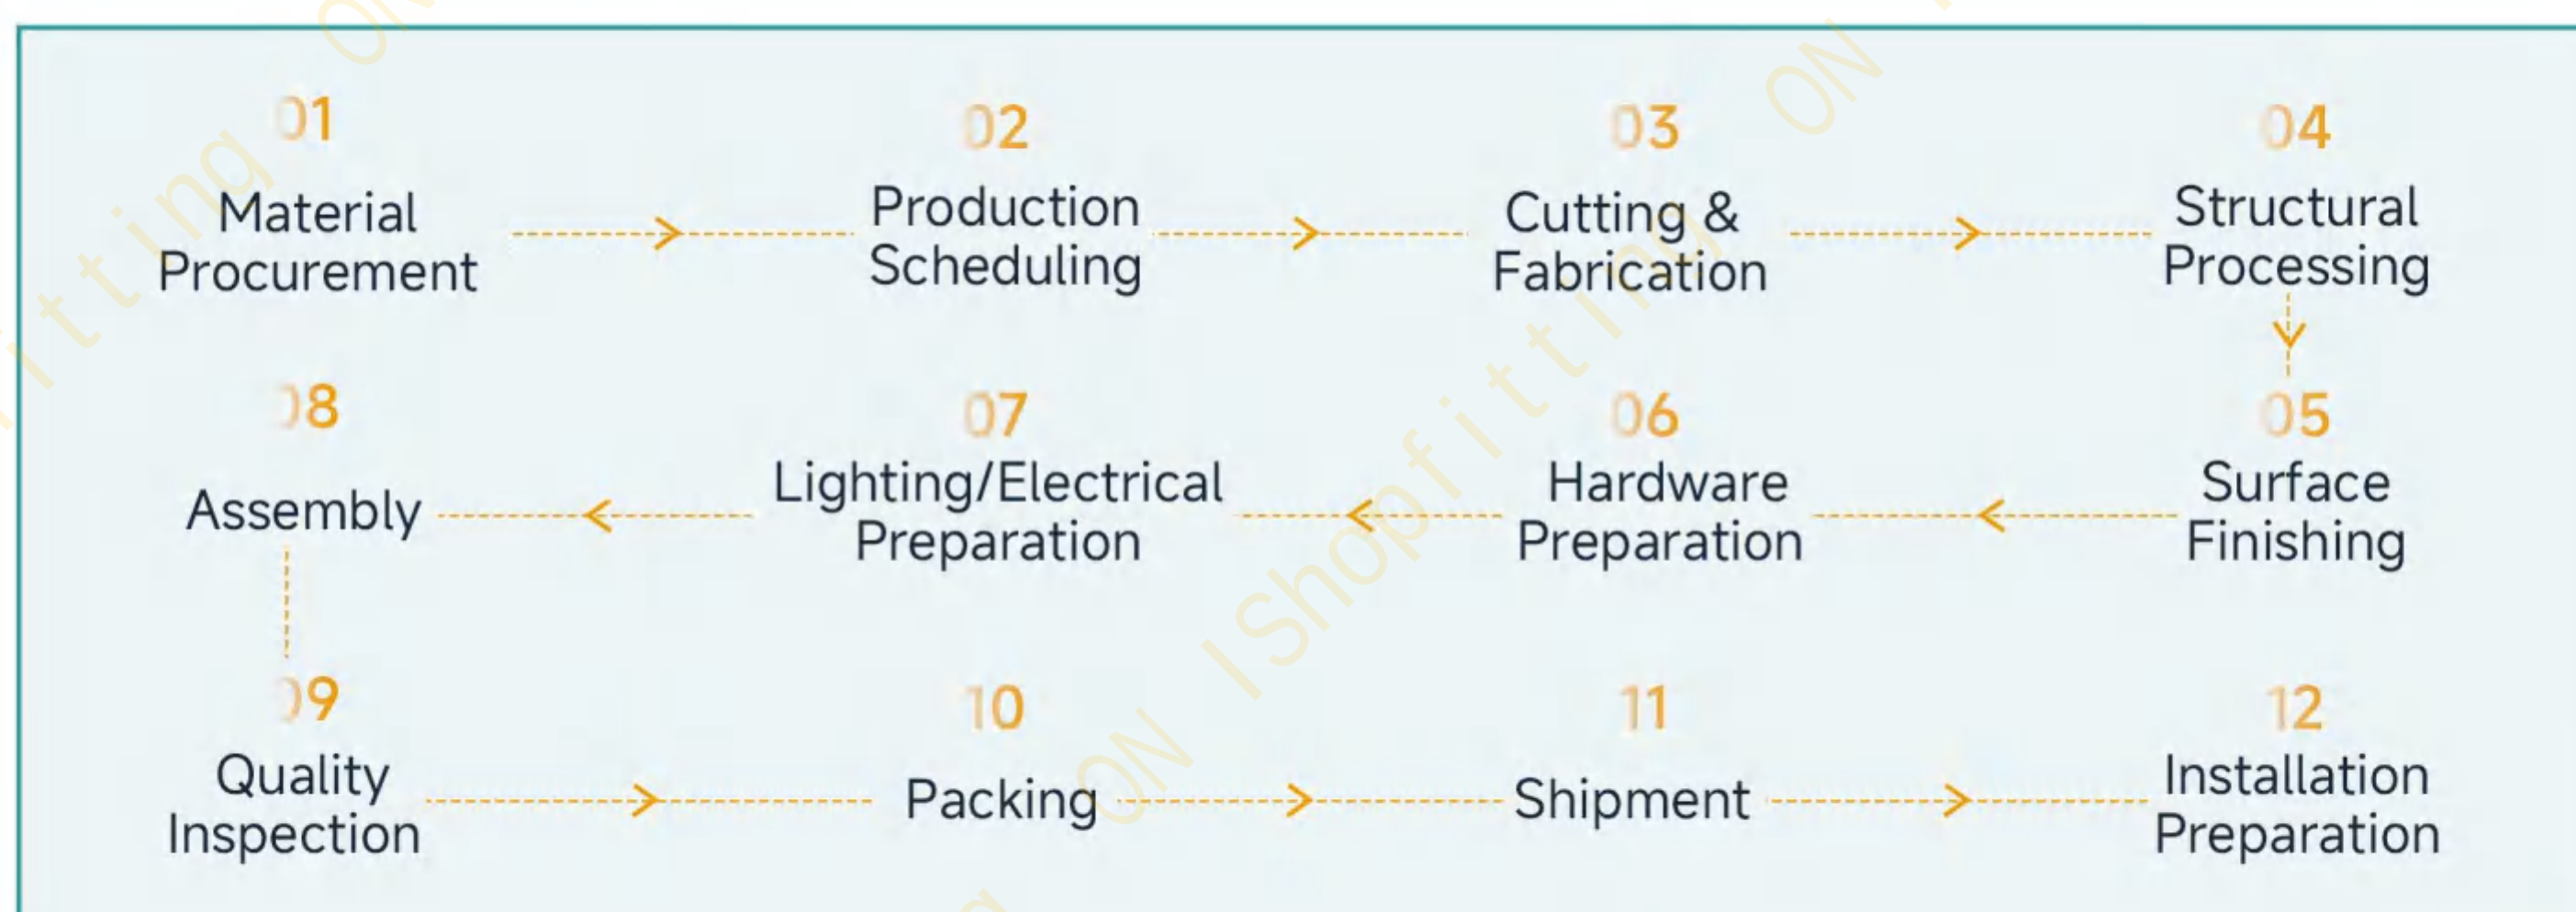

2. WHY CHANGES AFTER APPROVAL ARE DIFFICULT

Once drawings and materials have been approved and production has been released, changes should be avoided wherever possible. A post-approval change may affect the entire manufacturing and supply chain.

A. MATERIALS

Materials may already have been ordered, customized, cut, processed, painted, laminated or otherwise prepared specifically for the project.

- MDF, plywood and timber panels
- Veneer, laminate, paint and special finishes
- Stainless steel and other metal components
- Glass, acrylic, custom hardware, LED lighting and electrical components
- Special accessories and fittings

Project-specific materials often cannot be reused. If specifications change after procurement or cutting, materials may need to be scrapped and reordered, resulting in additional cost and lead time.

B. FACTORY PRODUCTION

After production release, the factory has allocated capacity, issued workshop orders, prepared cutting and fabrication schedules, assigned production teams and released technical drawings to multiple departments.

- Production may need to stop or be rescheduled
- Workshop drawings and instructions may need revision and reissue
- Fabrication procedures and the overall production sequence may be affected

C. ENGINEERING & QUALITY CONTROL

Structural details, welding methods, drilling positions, electrical layouts, load-bearing considerations, assembly methods and QC standards are prepared according to the approved drawings.

- Recalculate structures and revise fabrication drawings
- Update cutting, drilling, electrical and lighting information
- Update BOM/material lists and workshop documentation
- Revise QC inspection standards

Even a visually small change may require substantial technical work behind the scenes.

2. WHY CHANGES AFTER APPROVAL ARE DIFFICULT (CONTINUED)

D. PACKING, INSTALLATION & DELIVERY

Packing methods, packing lists, assembly instructions, installation drawings, fixing details and shipping documentation are prepared using the approved version.

- Packing dimensions, quantities and carton/crate configuration
- Container loading plans and shipping/export documentation
- Installation instructions, site fixing details, accessories and spare parts

If documents are not updated consistently, there is a risk of incorrect dimensions, mismatched components, missing accessories or installation difficulties on site.

E. PROJECT LEAD TIME

RE-PURCHASING

RE-PURCHASING

RE-PURCHASING

RE-FINISHING

RE-INSPECTION

RE-PACKING

Any post-approval modification may extend the agreed production and delivery schedule.

This is particularly important where the project has a fixed site installation date, store opening date, handover deadline or shipping schedule.

Please verify all details before approval. Changes after production release may result in additional cost and a revised completion date.

3. CHANGE REQUEST PROCEDURE AFTER APPROVAL

STEP 1

WRITTEN CHANGE REQUEST

The client must submit the requested changes in writing, clearly identifying affected item numbers, drawings, dimensions, materials, finishes or specifications.

STEP 2

ONI IMPACT ASSESSMENT

ONI will evaluate additional material costs, wastage, engineering/design effort, fabrication or labor, rework, packing changes, schedule impact and the revised delivery date.

STEP 3

WRITTEN CHANGE APPROVAL

ONI will issue the revised cost and/or production schedule for the client's written approval.

STEP 4

CHANGE IMPLEMENTATION

Only after both parties confirm the additional cost and revised schedule in writing will ONI implement the requested change.

Until written change approval is received, ONI will continue manufacturing according to the latest officially approved drawings and material specifications.

! Any issue resulting from information, dimensions, specifications or requirements approved by the client but subsequently changed without an agreed written change order shall not be considered a manufacturing defect or supplier responsibility.

4. PLEASE REVIEW CAREFULLY BEFORE APPROVAL

We strongly recommend one final internal review before approving the drawings. Please involve all relevant parties where necessary:

PROJECT MANAGER	DESIGNER	ARCHITECT	CONTRACTOR
SITE TEAM	ELECTRICAL TEAM	BRAND TEAM	PROCUREMENT TEAM

It is much easier, faster and less expensive to correct a detail before production starts than after materials have been purchased and manufacturing has begun.

Once everything has been carefully reviewed and confirmed, please return the signed drawings or provide written approval by email. Upon receiving your approval and the required payment, ONI will proceed with production accordingly.

CLIENT APPROVAL

We confirm that the drawings and material specifications have been reviewed and approved for production.

Authorized name:

Company:

Signature / stamp:

Date:



Thank you very much for your understanding and cooperation

Ms.CICI Tang

Sales & Marketing Director

-  Wechat: CICIChina2020
-  WhatsApp/Mobile: +86 18620963396
-  Email: sales1@onishopfitting.com
-  Website: onidisplay.com; onishopfitting.com
-  Factory Add.: ONI Factory, Xiusheng Road,
Taihe Town, Baiyun District, Guangzhou, China

